



SNAKE RIVER WATERSHED PLAN PARTNERSHIP

2025 ANNUAL PROGRESS REPORT FY 2024 (2024-2026) WORK PLAN



545 FT
NATIVE PLANT BUFFERS




1805 ACRES
WOODLAND STEWARDSHIP PLANS




3 LIVESTOCK BMP'S




1 WETLAND RESTORATION



2 WELL SEALINGS




2 SEPTIC UPGRADES



57% OF GOALS FOR THE FY24
WORK PLAN HAVE BEEN
ACCOMPLISHED

	GOAL: 107 LBS REDUCTION IN TOTAL PHOSPHORUS ACTUAL : 240 LBS PHOSPHORUS/YEAR ; 20 ENCUMBERED
	GOAL: 170 TON REDUCTION IN TOTAL SUSPENDED SOLIDS (TSS) ACTUAL : 293 TON TSS REDUCED
	GOAL: 5 OUTREACH DOCUMENTS OR DEMONSTRATIONS ACTUAL : >5 OUTREACH DOCUMENTS OR DEMONSTRATIONS
	GOAL: 1 ACRE FEET OF WETLANDS RESTORED ACTUAL : 31 ACRES OF WETLAND RESTORED
	GOAL: 800 FT OF BUFFERS INSTALLED ACTUAL : 545 FT OF BUFFER INSTALLED ; 100 ENCUMBERED
	GOAL: 3 UNUSED WELLS SEALED ACTUAL : 2 WELLS SEALED
	GOAL: 800 ACRES OF FOREST STEWARDSHIP PLANNING WRITTEN ACTUAL : 1805 ACRES PLANNED (19 PLANS)
	GOAL: 100 ACRES OF FORESTRY BEST MANAGEMENT PRACTICES ACTUAL : 4 ACRES INSTALLED (53.7 ACRES CONTRACTED)
	GOAL: 1 LIVESTOCK BMP INSTALLED ACTUAL : 1 INSTALLED (2 CONTRACTED)
	GOAL: 1 NUTRIENT MANAGEMENT PLAN COMPLETED ACTUAL : 0 PLANS COMPLETED (3 PLANS CONTRACTED)
	GOAL: INCREASE CAPACITY 1.5 FY FTE EMPLOYEES ACTUAL : 1.5 FY FTE EMPLOYEES
	GOAL: 3 SUB-WATERSHED ASSESSMENTS ACTUAL : 1 COMPLETED (1 FEASIBILITY STUDY CONTRACTED)
	GOAL: 70 OUTREACH CONTACT HOURS COMPLETED ACTUAL : ESTIMATED 70 CONTACT HOURS
	GOAL: 3 PRIVATE SEPTIC SYSTEMS BROUGHT INTO COMPLIANCE ACTUAL : 2 SSTS BUILT (1 ACTIVE APPLICATION)

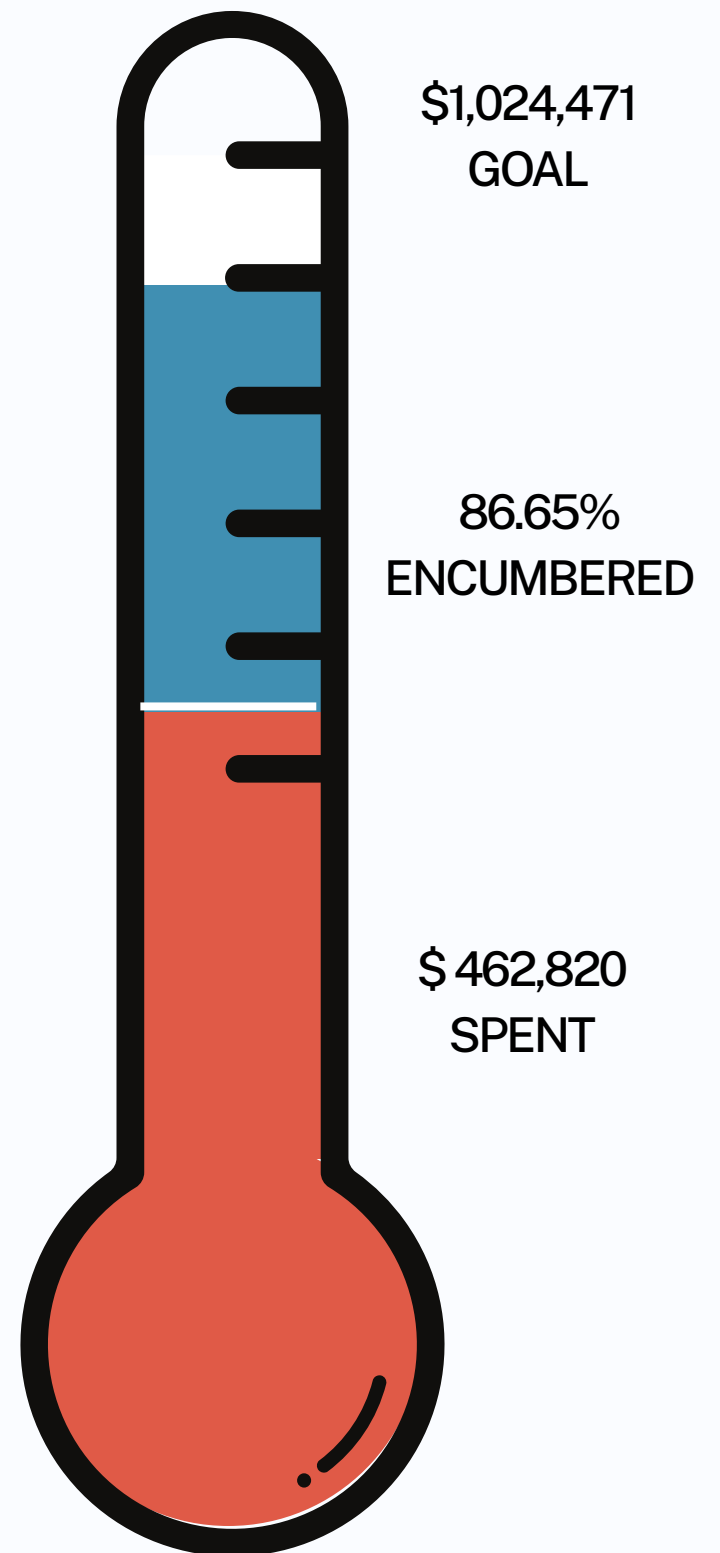

FY 24 WBIF Grant

