



# SNAKE RIVER WATERSHED PLAN PARTNERSHIP

## 2025 MID YEAR PROGRESS REPORT 2024-2025 WORK PLAN



**445 FT  
NATIVE PLANT BUFFERS**




**1139 ACRES  
WOODLAND STEWARDSHIP PLANS**




**3 LIVESTOCK BMP'S**




**1 WETLAND RESTORATION**



**2 WELL SEALINGS**




**1 SEPTIC UPGRADES**

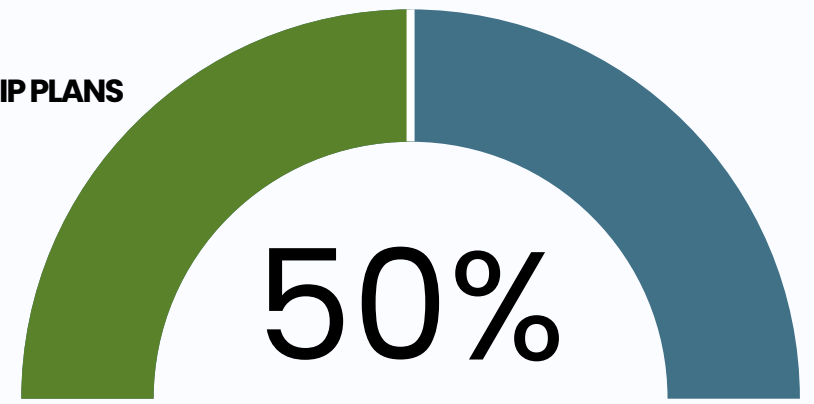

50 % OF GOALS FOR THE 2024-2025  
WORK PLAN HAVE BEEN  
ACCOMPLISHED

	GOAL: 107 LBS REDUCTION IN TOTAL PHOSPHORUS ACTUAL : 111 LBS PHOSPHORUS/ YEAR
	GOAL: 170 TON REDUCTION IN TOTAL SUSPENDED SOLIDS (TSS) ACTUAL : 187 TSS TONS/YEAR
	GOAL: 5 OUTREACH DOCUMENTS OR DEMONSTRATIONS ACTUAL : >5 OUTREACH DOCUMENTS OR DEMONSTRATIONS
	GOAL: 1 ACRE FEET OF WETLANDS RESTORED ACTUAL : 31 ACRES OF WETLAND RESTORED
	GOAL: 800 FT OF BUFFERS INSTALLED ACTUAL : 445 TOTAL FT OF BUFFER INSTALLED
	GOAL: 3 UNUSED WELLS SEALED ACTUAL : 1 WELL SEALED, 1 UNDER CONTRACT
	GOAL: 800 ACRES OF FOREST STEWARDSHIP PLANNING WRITTEN ACTUAL : 1139 ACRES PLANNED (10 PLANS)
	GOAL: 100 ACRES OF FORESTRY BEST MANAGEMENT PRACTICES ACTUAL : 0 ACRES INSTALLED ( 43 ACRES CONTRACTED )
	GOAL: 1 LIVESTOCK BMP INSTALLED ACTUAL : 1 INSTALLED (2 CONTRACTED)
	GOAL: 1 NUTRIENT MANAGEMENT PLAN COMPLETED ACTUAL : 0 PLANS COMPLETED (3 PLANS CONTRACTED)
	GOAL: INCREASE CAPACITY 1.5 FY FTE EMPLOYEES ACTUAL : 1.5 FY FTE EMPLOYEES
	GOAL: 3 SUB-WATERSHED ASSESSMENTS ACTUAL : 1 COMPLETED (1 FEASIBILITY STUDY CONTRACTED)
	GOAL: 70 OUTREACH CONTACT HOURS COMPLETED ACTUAL : ESTIMATED 50 CONTACT HOURS
	GOAL: 3 PRIVATE SEPTIC SYSTEMS BROUGHT INTO COMPLIANCE ACTUAL : 1 SSTS BUILT -MANY APPLICANTS OVER INCOME LIMIT



**FY 24 WBIF Grant**

